











# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.










ID	WBS		Task Name	Duration	Start	Finish	Predec	Resource Names
1								
2	1		<b>Willington Bank Leadership Training</b>	<b>148.75 days</b>	<b>Mon 5/2/05</b>	<b>Thu 12/1/05</b>		
3								
4	1.1		<b>Kick-off Meeting</b>	<b>4.25 days</b>	<b>Mon 5/2/05</b>	<b>Fri 5/6/05</b>		
5	1.1.1		Develop Meeting agenda	0.25 days	Mon 5/2/05	Mon 5/2/05		Project Manager
6	1.1.2		Conduct QA Review of Agenda	0.25 days	Mon 5/2/05	Mon 5/2/05	5	QA Team
7	1.1.3		Submit Meeting Agenda to Client	0.25 days	Mon 5/2/05	Mon 5/2/05	6	Project Manager
8	1.1.4		Setup/Schedule Meeting	1 day	Mon 5/2/05	Tue 5/3/05	7	Project Manager
9	1.1.5		Conduct Meeting	0.5 days	Tue 5/3/05	Wed 5/4/05	8	Project Manager
10	1.1.6		Develop Meeting Minutes	1 day	Wed 5/4/05	Thu 5/5/05	9	Instructional Designer
11	1.1.7		Conduct QA Review	0.5 days	Thu 5/5/05	Thu 5/5/05	10	QA Team
12	1.1.8		Review QA Report	0.25 days	Thu 5/5/05	Thu 5/5/05	11	Project Manager
13	1.1.9		<b>Submit to Client</b>	<b>0.25 days</b>	<b>Fri 5/6/05</b>	<b>Fri 5/6/05</b>	<b>12</b>	<b>Project Manager</b>
14								
15	1.2		<b>Develop Learning Analysis Report</b>	<b>13.75 days</b>	<b>Fri 5/6/05</b>	<b>Wed 5/25/05</b>	<b>13</b>	
16	1.2.1		Develop Goal Statement	0.25 days	Fri 5/6/05	Fri 5/6/05		Instructional Designer
17	1.2.2		Conduct Goal Analysis	0.5 days	Fri 5/6/05	Fri 5/6/05	16	Instructional Designer
18	1.2.3		Conduct Subordinate Skills Analysis	1 day	Mon 5/9/05	Mon 5/9/05	17	Instructional Designer
19	1.2.4		Conduct Learner Analysis	2 days	Tue 5/10/05	Wed 5/11/05	18	Instructional Designer
20	1.2.5		Conduct Learning Environment Analysis	2 days	Thu 5/12/05	Fri 5/13/05	19	Instructional Designer
21	1.2.6		Define Performance Objectives	0.5 days	Mon 5/16/05	Mon 5/16/05	20	Instructional Designer
22	1.2.7		Identify Assessment Approach	0.25 days	Mon 5/16/05	Mon 5/16/05	21	Instructional Designer
23	1.2.8		Compile Learning Analysis Report	1 day	Mon 5/16/05	Tue 5/17/05	22	Instructional Designer
24	1.2.9		Conduct QA Review	1 day	Tue 5/17/05	Wed 5/18/05	23	QA Team
25	1.2.10		Review QA Report	1 day	Wed 5/18/05	Thu 5/19/05	24	Project Manager
26	1.2.11		<b>Submit to Client</b>	<b>0.25 days</b>	<b>Thu 5/19/05</b>	<b>Thu 5/19/05</b>	<b>25</b>	<b>Project Manager</b>

Project: project schedule Date: Wed 4/6/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.










ID	WBS		Task Name	Duration	Start	Finish	Predec	Resource Names
27	1.2.12		<b>Client Review Period</b>	3 days	Fri 5/20/05	Tue 5/24/05	26	Client
28	1.2.13		Review & Incorporate Client Feedback	1 day	Wed 5/25/05	Wed 5/25/05	27	Project Manager
29	1.2.14		Conduct QA Review	1 day	Fri 5/6/05	Mon 5/9/05		QA Team
30								
31	1.3		<b>Develop Design Plan</b>	12.5 days	Wed 5/25/05	Mon 6/13/05	27	
32	1.3.1		Define Learner Assessment Approach	2 days	Wed 5/25/05	Thu 5/26/05		Instructional Designer
33	1.3.2		Identify Instructional Strategy	1 day	Fri 5/27/05	Fri 5/27/05	32	Instructional Designer
34	1.3.3		Identify Level of Interaction	0.25 days	Tue 5/31/05	Tue 5/31/05	33	Instructional Designer
35	1.3.4		Identify Media	1 day	Tue 5/31/05	Wed 6/1/05	34	Instructional Designer
36	1.3.5		Compile Design Plan	2 days	Wed 6/1/05	Fri 6/3/05	35	Instructional Designer
37	1.3.6		Conduct QA Review	1 day	Fri 6/3/05	Mon 6/6/05	36	QA Team
38	1.3.7		Review QA Report	1 day	Mon 6/6/05	Tue 6/7/05	37	Project Manager
39	1.3.8		<b>Submit to Client</b>	0.25 days	Tue 6/7/05	Tue 6/7/05	38	Project Manager
40	1.3.9		<b>Client Review Period</b>	3 days	Tue 6/7/05	Fri 6/10/05	39	Client
41	1.3.10		Review & Incorporate Client Feedback	1 day	Fri 6/10/05	Mon 6/13/05	40	Project Manager
42	1.3.11		Conduct QA Review	1 day	Wed 5/25/05	Wed 5/25/05		QA Team
43								
44	1.4		<b>Develop Static Prototype</b>	10.5 days	Mon 6/13/05	Mon 6/27/05	41	
45	1.4.1		Design Storyboard	1 day	Mon 6/13/05	Tue 6/14/05		Instructional Designer
46	1.4.2		Design Interface Layout	1 day	Tue 6/14/05	Wed 6/15/05	45	Instructional Designer
47	1.4.3		Create Artwork	1 day	Wed 6/15/05	Thu 6/16/05	46	Graphic Designer
48	1.4.4		Develop Static Prototype	1 day	Thu 6/16/05	Fri 6/17/05	47	Web Developer
49	1.4.5		Conduct QA Review	1 day	Fri 6/17/05	Mon 6/20/05	48	QA Team
50	1.4.6		Review QA Report	0.25 days	Mon 6/20/05	Mon 6/20/05	49	Project Manager
51	1.4.7		<b>Submit to Client</b>	0.25 days	Mon 6/20/05	Mon 6/20/05	50	Project Manager
52	1.4.8		<b>Client Review Period</b>	3 days	Tue 6/21/05	Thu 6/23/05	51	Client

Project: project schedule Date: Wed 4/6/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.










ID	WBS		Task Name	Duration	Start	Finish	Predec	Resource Names
53	1.4.9		Review & Incorporate Client Feedback	2 days	Fri 6/24/05	Mon 6/27/05	52	Project Manager
54	1.4.10		Conduct QA Review	1 day	Mon 6/13/05	Tue 6/14/05		QA Team
55								
56	<b>1.5</b>		<b>Develop Functional Prototype</b>	<b>24.25 days</b>	<b>Tue 6/28/05</b>	<b>Tue 8/2/05</b>	<b>53</b>	
57	1.5.1		Identify Objectives	0.5 days	Tue 6/28/05	Tue 6/28/05		Instructional Designer
58	1.5.2		Identify Content	1 day	Tue 6/28/05	Wed 6/29/05	57	SME
59	1.5.3		Develop Content	2 days	Wed 6/29/05	Fri 7/1/05	58	Instructional Designer
60	1.5.4		Develop Storyboard	1 day	Fri 7/1/05	Tue 7/5/05	59	Instructional Designer
61	1.5.5		Develop Artwork	2 days	Tue 7/5/05	Thu 7/7/05	60	Graphic Designer
62	1.5.6		Develop Media	3 days	Thu 7/7/05	Tue 7/12/05	61	Graphic Designer
63	1.5.7		Program Prototype	5 days	Tue 7/12/05	Tue 7/19/05	62	Programmer
64	1.5.8		Conduct QA Review	3 days	Tue 7/19/05	Fri 7/22/05	63	QA Team
65	1.5.9		Review QA Report	0.5 days	Fri 7/22/05	Fri 7/22/05	64	Project Manager
66	<b>1.5.10</b>		<b>Submit to Client</b>	<b>0.25 days</b>	<b>Mon 7/25/05</b>	<b>Mon 7/25/05</b>	<b>65</b>	<b>Project Manager</b>
67	<b>1.5.11</b>		<b>Client Review Period</b>	<b>3 days</b>	<b>Mon 7/25/05</b>	<b>Thu 7/28/05</b>	<b>66</b>	<b>Client</b>
68	1.5.12		Review & Incorporate Client Feedback	2 days	Thu 7/28/05	Mon 8/1/05	67	Project Manager
69	1.5.13		Conduct QA Review	1 day	Mon 8/1/05	Tue 8/2/05	68	QA Team
70								
71	<b>1.6</b>		<b>Conduct Usability Testing</b>	<b>3 days</b>	<b>Mon 8/1/05</b>	<b>Thu 8/4/05</b>	<b>68</b>	
72	1.6.1		Identify Usability Group	0.5 days	Mon 8/1/05	Mon 8/1/05		Project Manager
73	1.6.2		Conduct Usability Study	1 day	Mon 8/1/05	Tue 8/2/05	72	QA Team
74	1.6.3		Review Results	0.5 days	Tue 8/2/05	Wed 8/3/05	73	Project Manager
75	1.6.4		Update Design Plan	1 day	Wed 8/3/05	Thu 8/4/05	74	Instructional Designer
76								
77	<b>1.7</b>		<b>Develop Final Product</b>	<b>58.25 days</b>	<b>Thu 8/4/05</b>	<b>Wed 10/26/05</b>	<b>75</b>	
78	1.7.1		Identify Objectives	1 day	Thu 8/4/05	Fri 8/5/05		Instructional Designer

Project: project schedule Date: Wed 4/6/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

ID	WBS		Task Name	Duration	Start	Finish	Predec	Resource Names
79	1.7.2		Identify Content	1 day	Fri 8/5/05	Mon 8/8/05	78	SME
80	1.7.3		Develop Content	4 days	Mon 8/8/05	Fri 8/12/05	79	Instructional Designer
81	1.7.4		Develop Storyboard	2 days	Fri 8/12/05	Tue 8/16/05	80	Instructional Designer
82	1.7.5		Develop Artwork	5 days	Tue 8/16/05	Tue 8/23/05	81	Graphic Designer
83	1.7.6		Develop Media	5 days	Tue 8/23/05	Tue 8/30/05	82	Graphic Designer
84	1.7.7		Program Final Product	10 days	Tue 8/30/05	Wed 9/14/05	83	Programmer
85	1.7.8		Conduct QA Review	5 days	Wed 9/14/05	Wed 9/21/05	84	QA Team
86	1.7.9		Review QA Report	1 day	Wed 9/21/05	Thu 9/22/05	85	Project Manager
87	<b>1.7.10</b>		<b>Submit to Client</b>	<b>0.25 days</b>	<b>Thu 9/22/05</b>	<b>Thu 9/22/05</b>	<b>86</b>	<b>Project Manager</b>
88	<b>1.7.11</b>		<b>Client Review Period</b>	<b>20 days</b>	<b>Thu 9/22/05</b>	<b>Thu 10/20/05</b>	<b>87</b>	<b>Client</b>
89	1.7.12		Review & Incorporate Client Feedback	3 days	Thu 10/20/05	Tue 10/25/05	88	Project Manager
90	1.7.13		Conduct QA Review	1 day	Tue 10/25/05	Wed 10/26/05	89	QA Team
91								
92	<b>1.8</b>		<b>Translate Final Product</b>	<b>20.25 days</b>	<b>Tue 10/25/05</b>	<b>Tue 11/22/05</b>	<b>89</b>	
93	1.8.1		Translate Content	5 days	Tue 10/25/05	Tue 11/1/05		Spanish Translator
94	1.8.2		Program Content	3 days	Tue 11/1/05	Fri 11/4/05	93	Programmer
95	1.8.3		Conduct QA Review	2 days	Fri 11/4/05	Tue 11/8/05	94	QA Team
96	1.8.4		Review QA Report	1 day	Tue 11/8/05	Wed 11/9/05	95	Project Manager
97	<b>1.8.5</b>		<b>Submit to Client</b>	<b>0.25 days</b>	<b>Wed 11/9/05</b>	<b>Wed 11/9/05</b>	<b>96</b>	<b>Project Manager</b>
98	<b>1.8.6</b>		<b>Client Review Period</b>	<b>5 days</b>	<b>Wed 11/9/05</b>	<b>Wed 11/16/05</b>	<b>97</b>	<b>Client</b>
99	1.8.7		Review & Incorporate Client Feedback	3 days	Wed 11/16/05	Mon 11/21/05	98	Project Manager
100	1.8.8		Conduct QA Review	1 day	Mon 11/21/05	Tue 11/22/05	99	QA Team
101								
102	1.9		<b>Implement Final Product</b>	<b>5 days</b>	<b>Tue 11/22/05</b>	<b>Thu 12/1/05</b>	<b>100</b>	Project Manager, Programm

Project: project schedule Date: Wed 4/6/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.



<p>Project: project schedule Date: Wed 4/6/05</p>	<p>Task </p> <p>Split </p> <p>Progress </p>	<p>Milestone </p> <p>Summary </p> <p>Project Summary </p>	<p>External Tasks </p> <p>External Milestone </p> <p>Deadline </p>
---	---	---	--

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.



Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="width: 20%;">Task</td> <td style="width: 20%;"></td> <td style="width: 20%;">Milestone</td> <td style="width: 20%;"></td> <td style="width: 20%;">External Tasks</td> <td></td> </tr> <tr> <td>Split</td> <td></td> <td>Summary</td> <td></td> <td>External Milestone</td> <td></td> </tr> <tr> <td>Progress</td> <td></td> <td>Project Summary</td> <td></td> <td>Deadline</td> <td></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.




























Mar 27, '05			Apr 3, '05				Apr 10, '05					Apr 17, '05					Apr 24, '05					May 1, '05				Ma												
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="padding: 2px;">Task</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Milestone</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">External Tasks</td> <td style="padding: 2px;"></td> </tr> <tr> <td style="padding: 2px;">Split</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Summary</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">External Milestone</td> <td style="padding: 2px;"></td> </tr> <tr> <td style="padding: 2px;">Progress</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Project Summary</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Deadline</td> <td style="padding: 2px;"></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

Mar 27, '05			Apr 3, '05				Apr 10, '05					Apr 17, '05					Apr 24, '05					May 1, '05				Ma												
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Task</td> <td style="width: 15%;"></td> <td style="width: 15%;">Milestone</td> <td style="width: 15%;"></td> <td style="width: 15%;">External Tasks</td> <td style="width: 20%;"></td> </tr> <tr> <td>Split</td> <td></td> <td>Summary</td> <td></td> <td>External Milestone</td> <td></td> </tr> <tr> <td>Progress</td> <td></td> <td>Project Summary</td> <td></td> <td>Deadline</td> <td></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

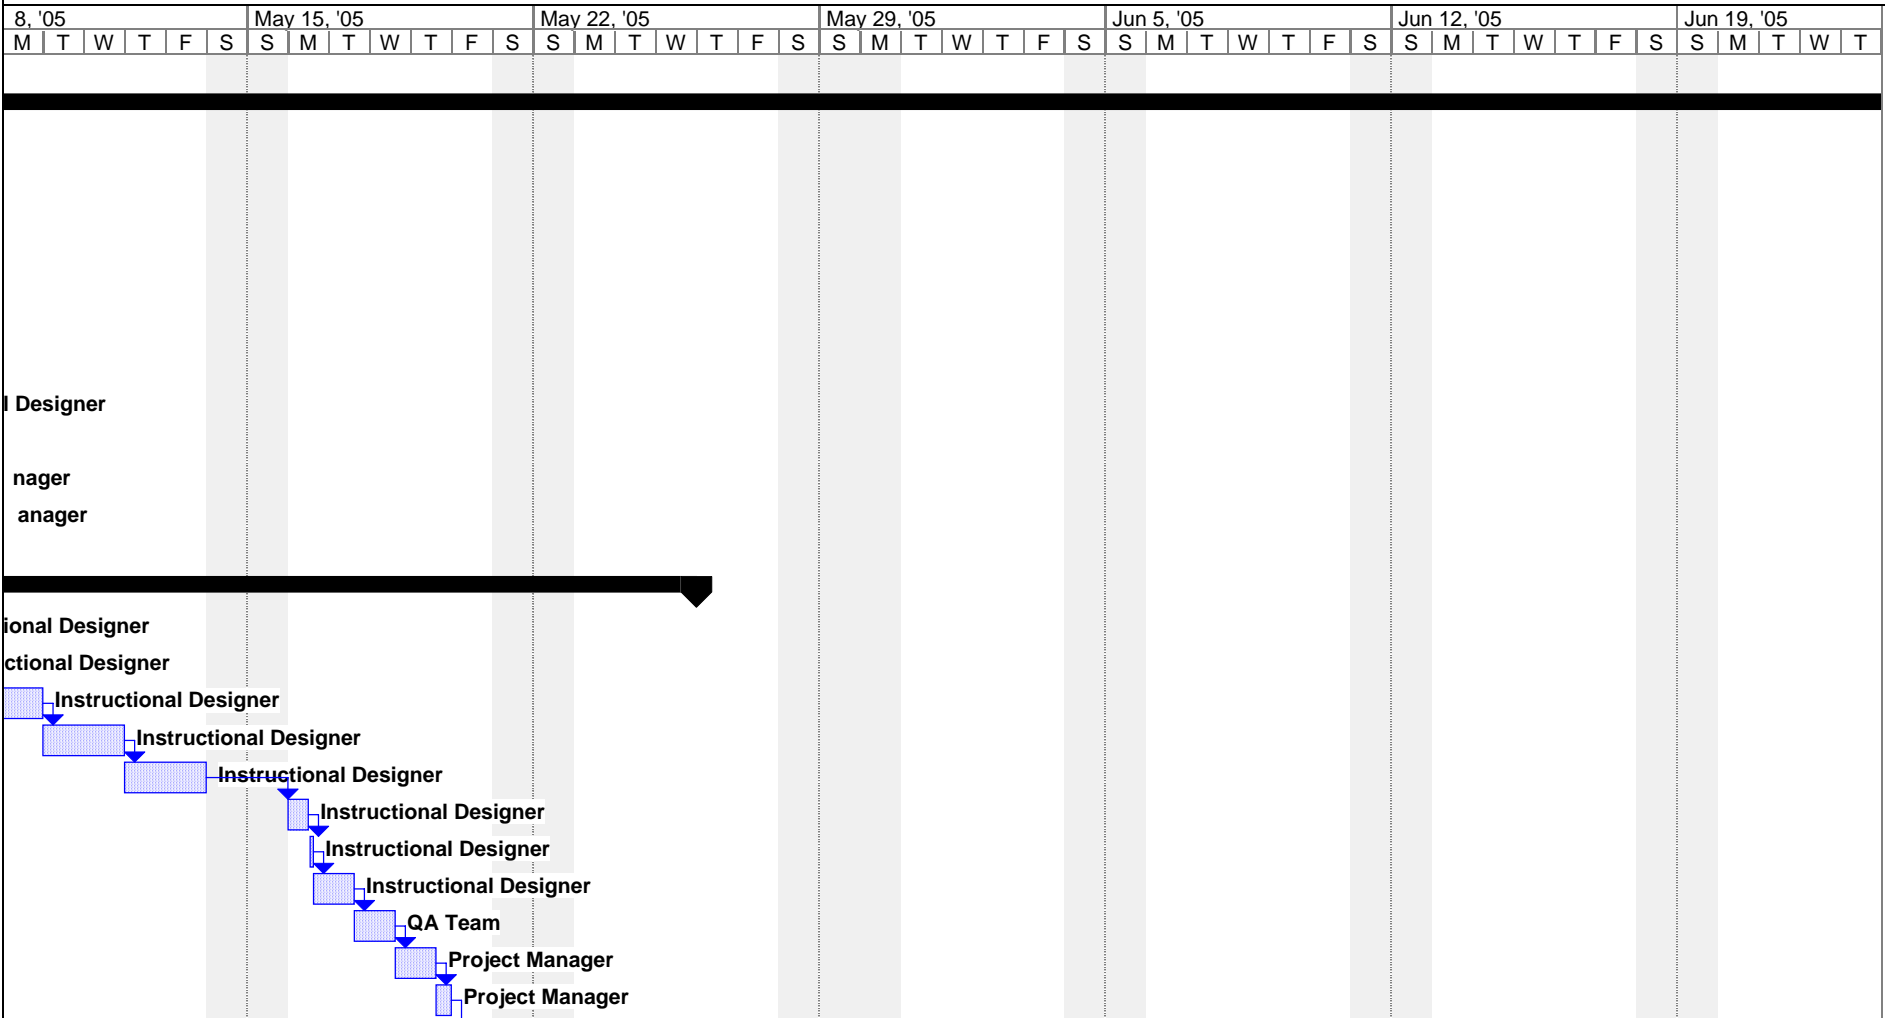

Project: project schedule Date: Wed 4/6/05	Task	Milestone	External Tasks
Split	Summary	External Milestone	Deadline
Progress	Project Summary		

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

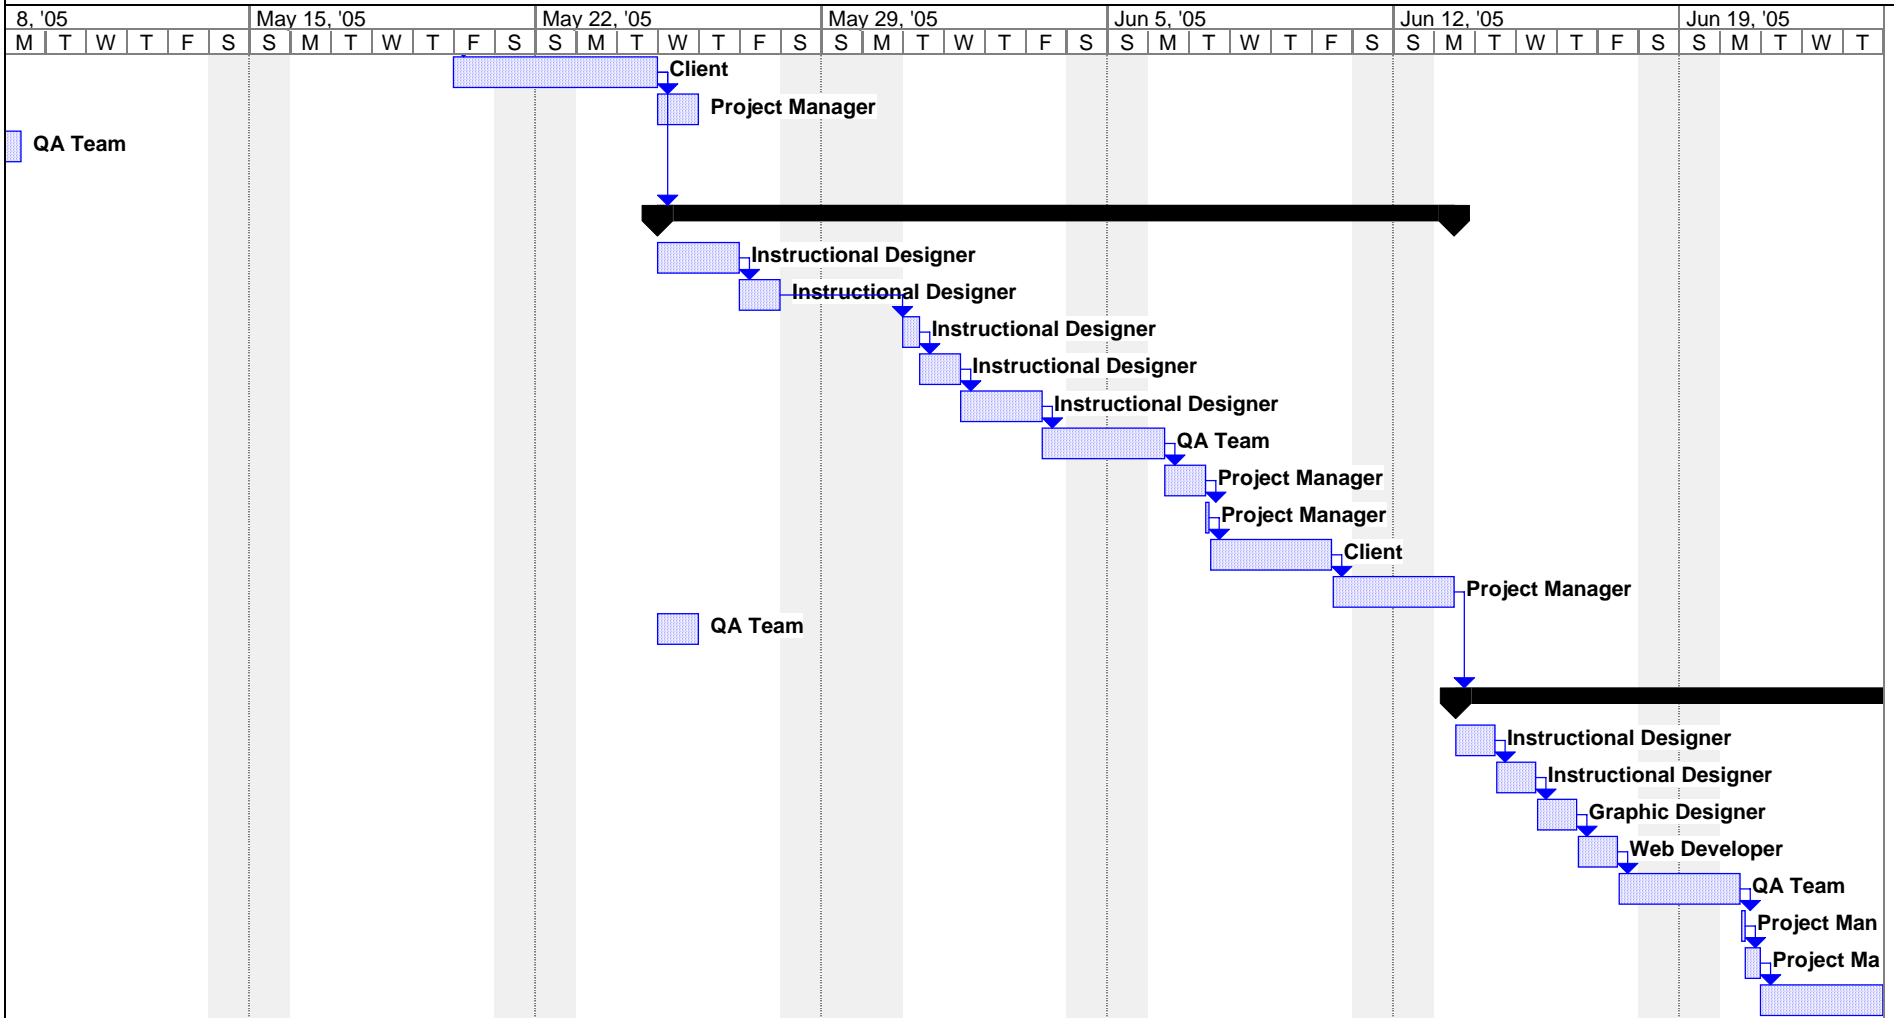







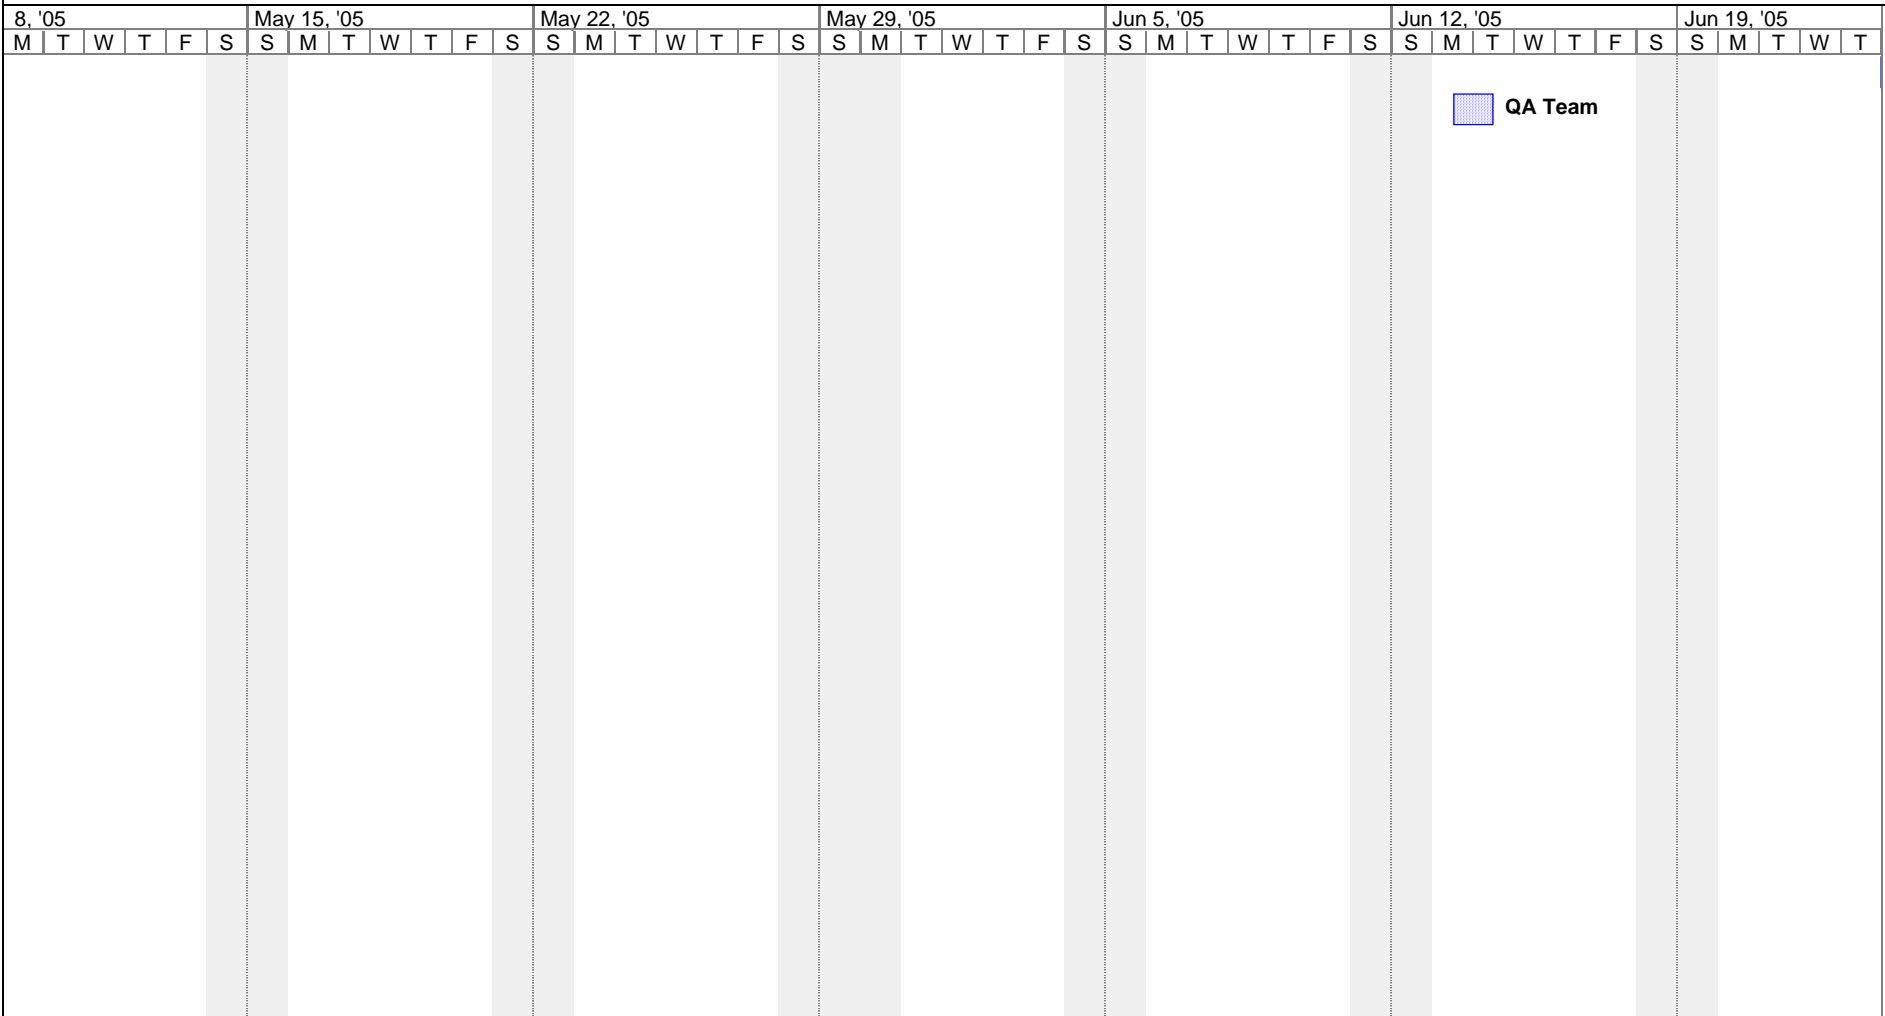


Project: project schedule Date: Wed 4/6/05	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.






























Project: project schedule Date: Wed 4/6/05	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

8, '05							May 15, '05							May 22, '05							May 29, '05							Jun 5, '05							Jun 12, '05							Jun 19, '05						
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T			

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Task</td> <td style="width: 15%;"></td> <td style="width: 15%;">Milestone</td> <td style="width: 15%;"></td> <td style="width: 15%;">External Tasks</td> <td style="width: 15%;"></td> </tr> <tr> <td>Split</td> <td></td> <td>Summary</td> <td></td> <td>External Milestone</td> <td></td> </tr> <tr> <td>Progress</td> <td></td> <td>Project Summary</td> <td></td> <td>Deadline</td> <td></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

Jun 26, '05					Jul 3, '05					Jul 10, '05					Jul 17, '05					Jul 24, '05					Jul 31, '05					Aug 7, '05								
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="padding: 2px;">Task</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Milestone</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">External Tasks</td> <td style="padding: 2px;"></td> </tr> <tr> <td style="padding: 2px;">Split</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Summary</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">External Milestone</td> <td style="padding: 2px;"></td> </tr> <tr> <td style="padding: 2px;">Progress</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Project Summary</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Deadline</td> <td style="padding: 2px;"></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

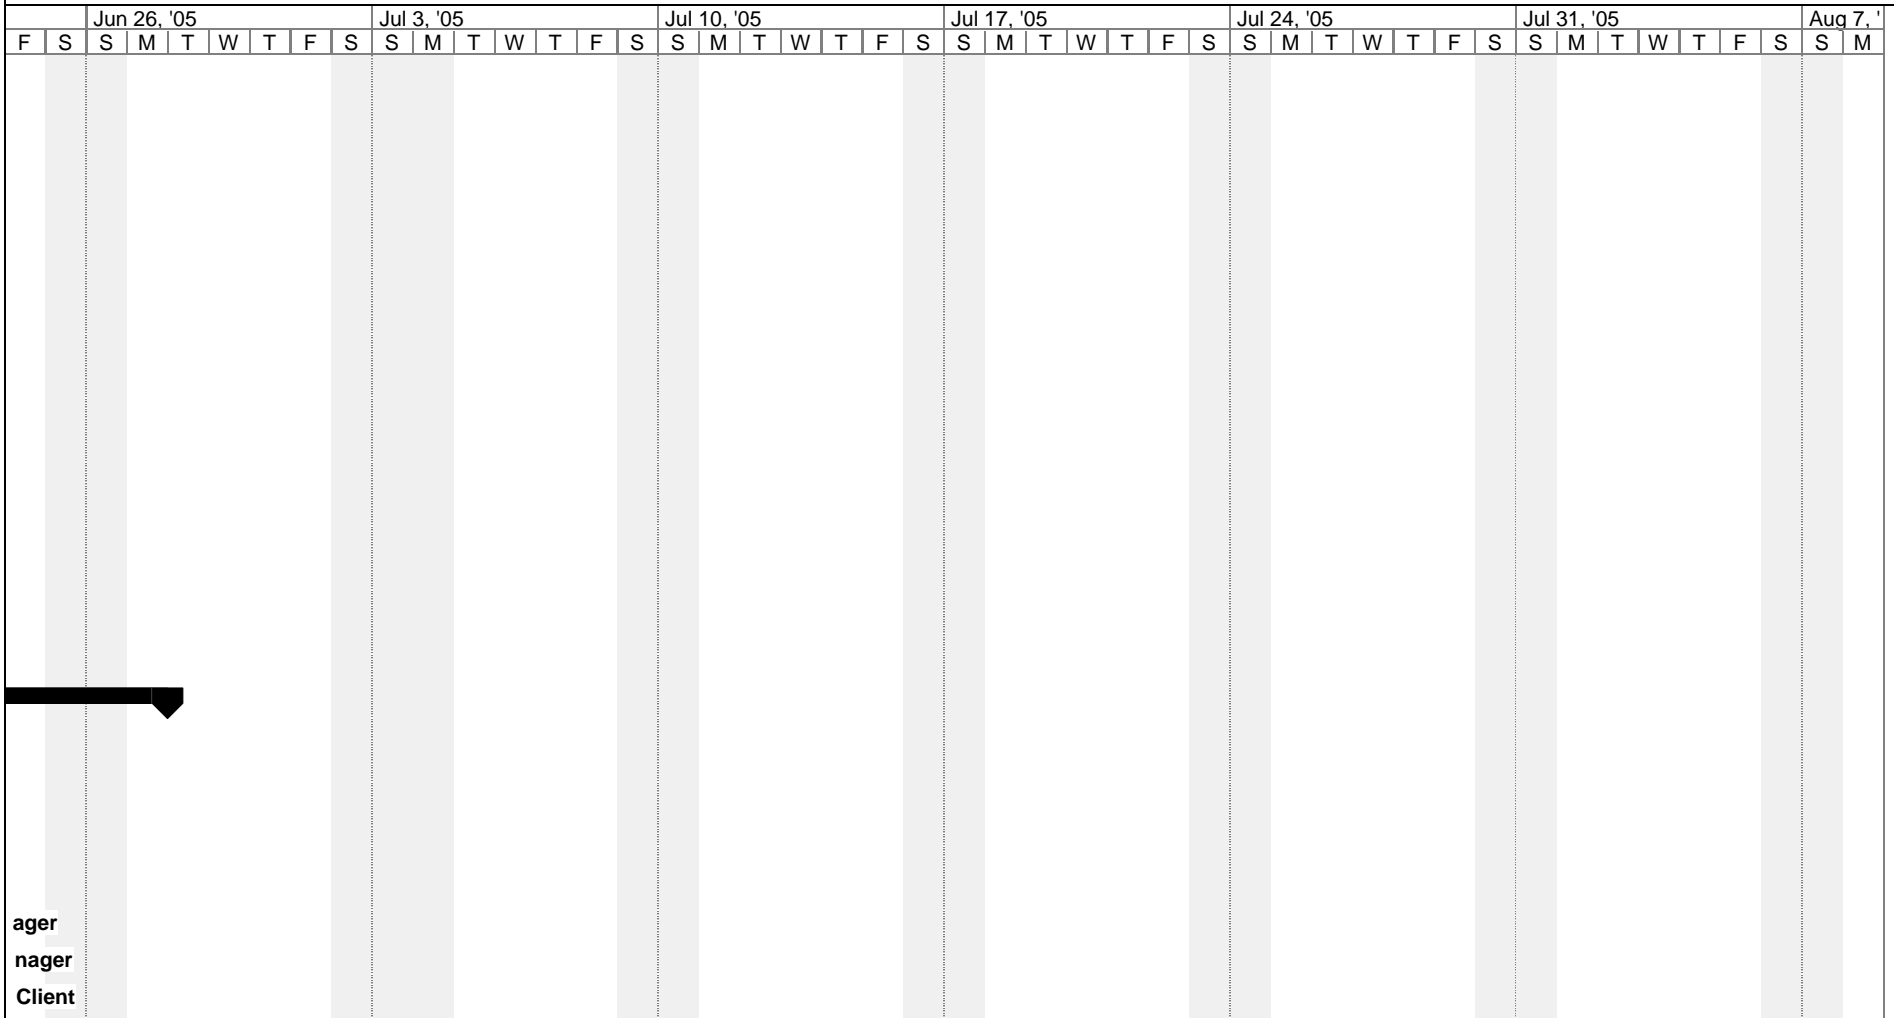

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="padding: 2px;">Task</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Milestone</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">External Tasks</td> <td style="padding: 2px;"></td> </tr> <tr> <td style="padding: 2px;">Split</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Summary</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">External Milestone</td> <td style="padding: 2px;"></td> </tr> <tr> <td style="padding: 2px;">Progress</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Project Summary</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Deadline</td> <td style="padding: 2px;"></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

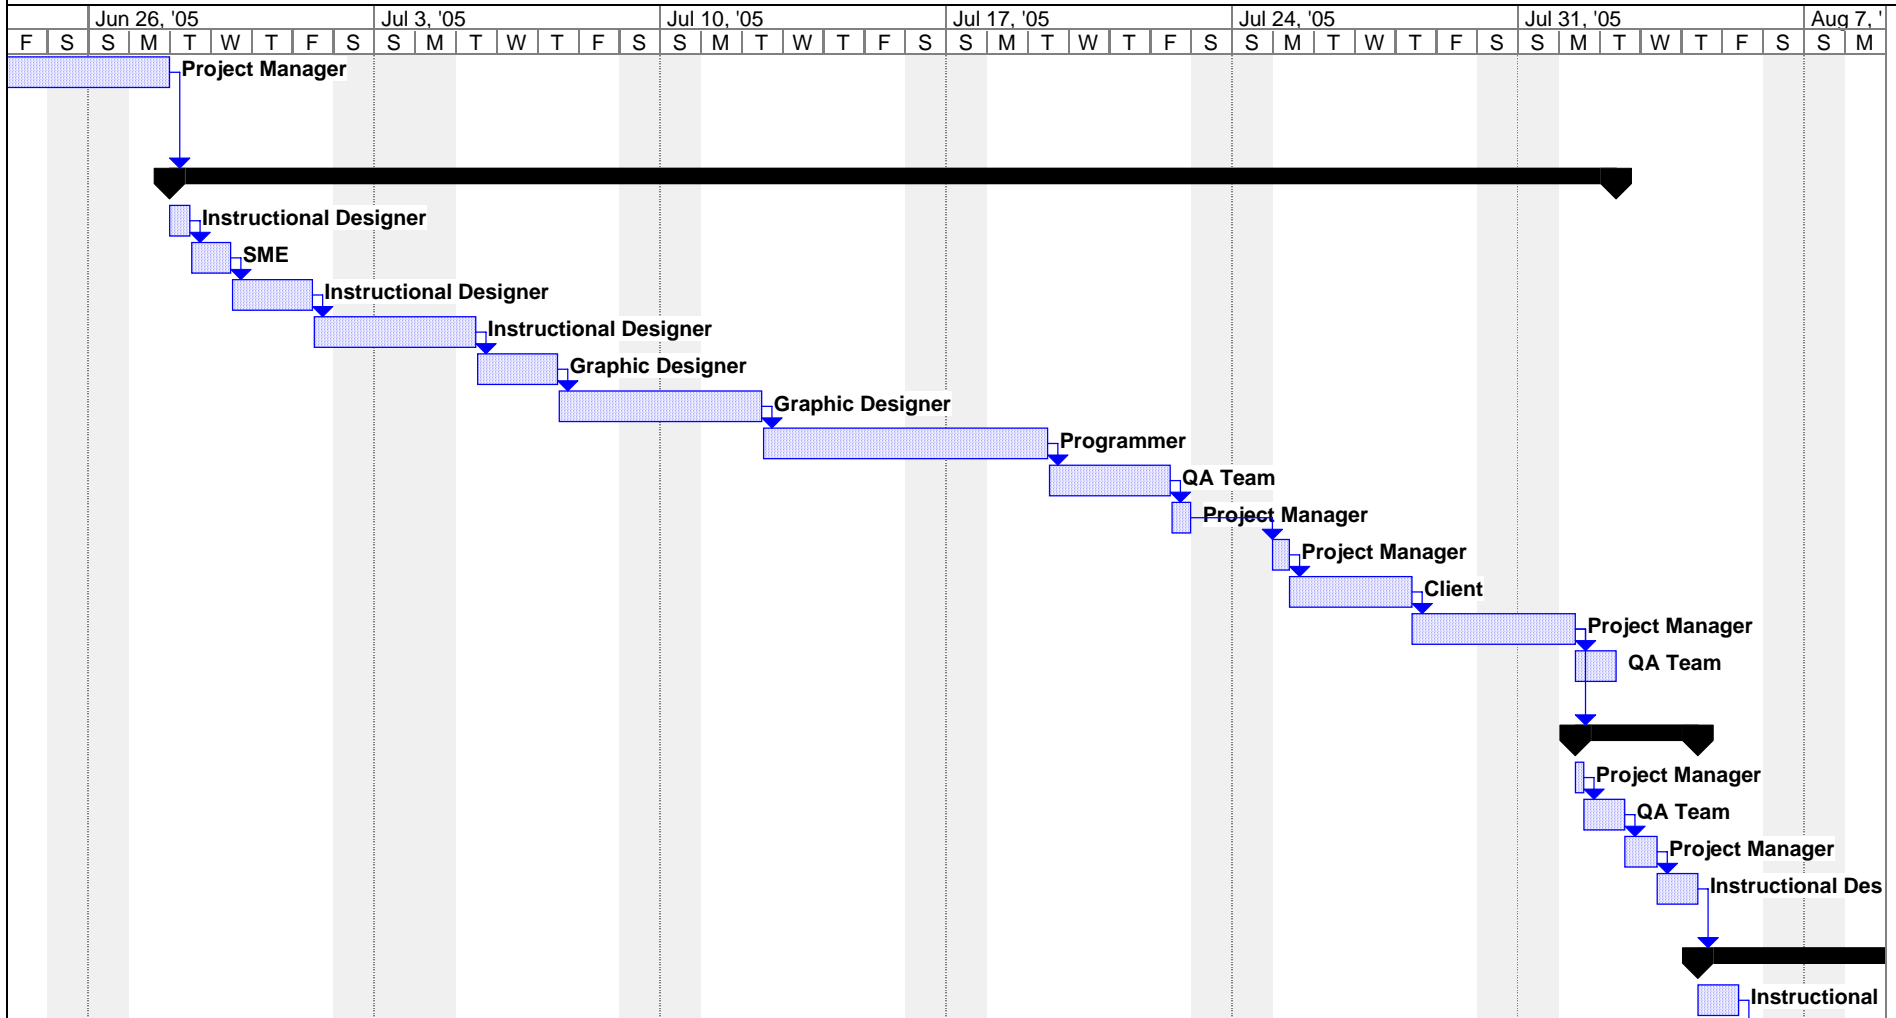

Project: project schedule Date: Wed 4/6/05	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

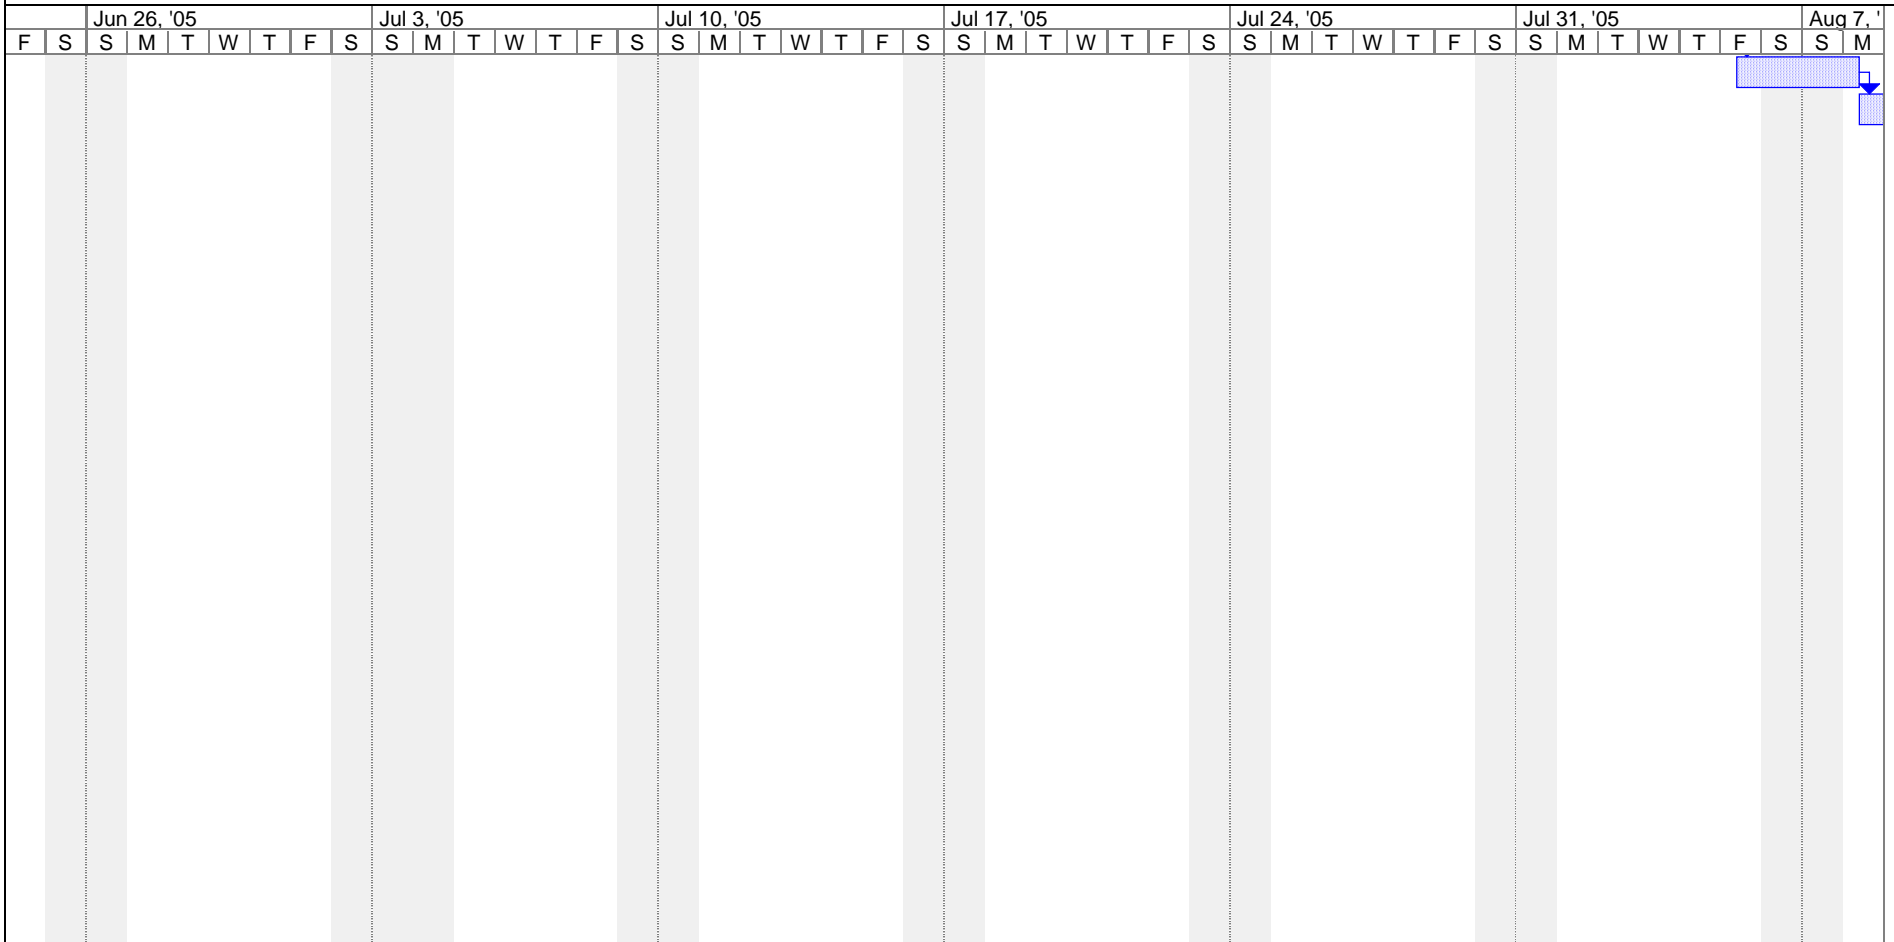

<p>Project: project schedule Date: Wed 4/6/05</p>	<p>Task </p>	<p>Milestone </p>	<p>External Tasks </p>
	<p>Split </p>	<p>Summary </p>	<p>External Milestone </p>
	<p>Progress </p>	<p>Project Summary </p>	<p>Deadline </p>

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

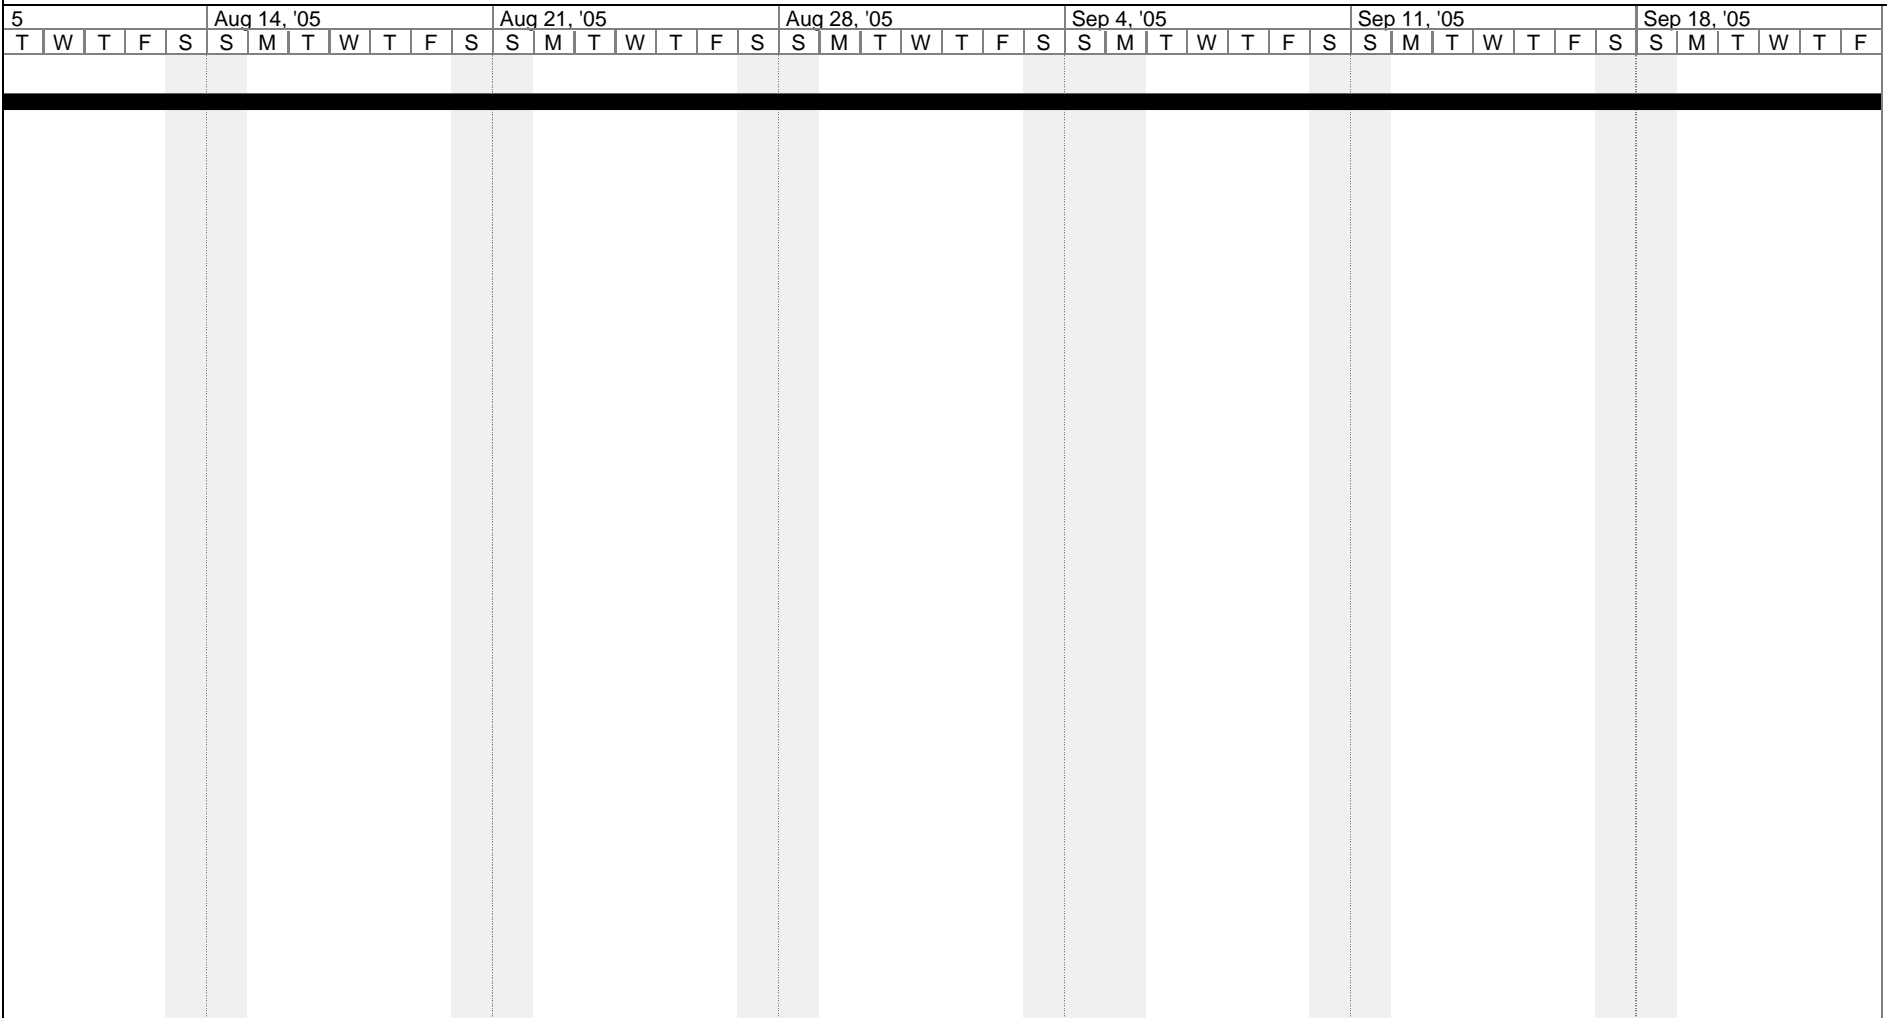

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Task</td> <td style="width: 15%;"></td> <td style="width: 15%;">Milestone</td> <td style="width: 15%;"></td> <td style="width: 15%;">External Tasks</td> <td style="width: 15%;"></td> </tr> <tr> <td>Split</td> <td></td> <td>Summary</td> <td></td> <td>External Milestone</td> <td></td> </tr> <tr> <td>Progress</td> <td></td> <td>Project Summary</td> <td></td> <td>Deadline</td> <td></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

5					Aug 14, '05					Aug 21, '05					Aug 28, '05					Sep 4, '05					Sep 11, '05					Sep 18, '05											
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		

Project: project schedule Date: Wed 4/6/05	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

5	Aug 14, '05					Aug 21, '05					Aug 28, '05					Sep 4, '05					Sep 11, '05					Sep 18, '05													
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
<div style="position: absolute; top: 50px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 100px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 150px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 200px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 250px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 300px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 350px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 400px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 450px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 500px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 550px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 600px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 650px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 700px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 750px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 800px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 850px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 900px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div> <div style="position: absolute; top: 950px; left: 50px; width: 100px; height: 20px; background-color: #cccccc;"></div>																																							


signer

Designer

Project: project schedule Date: Wed 4/6/05	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

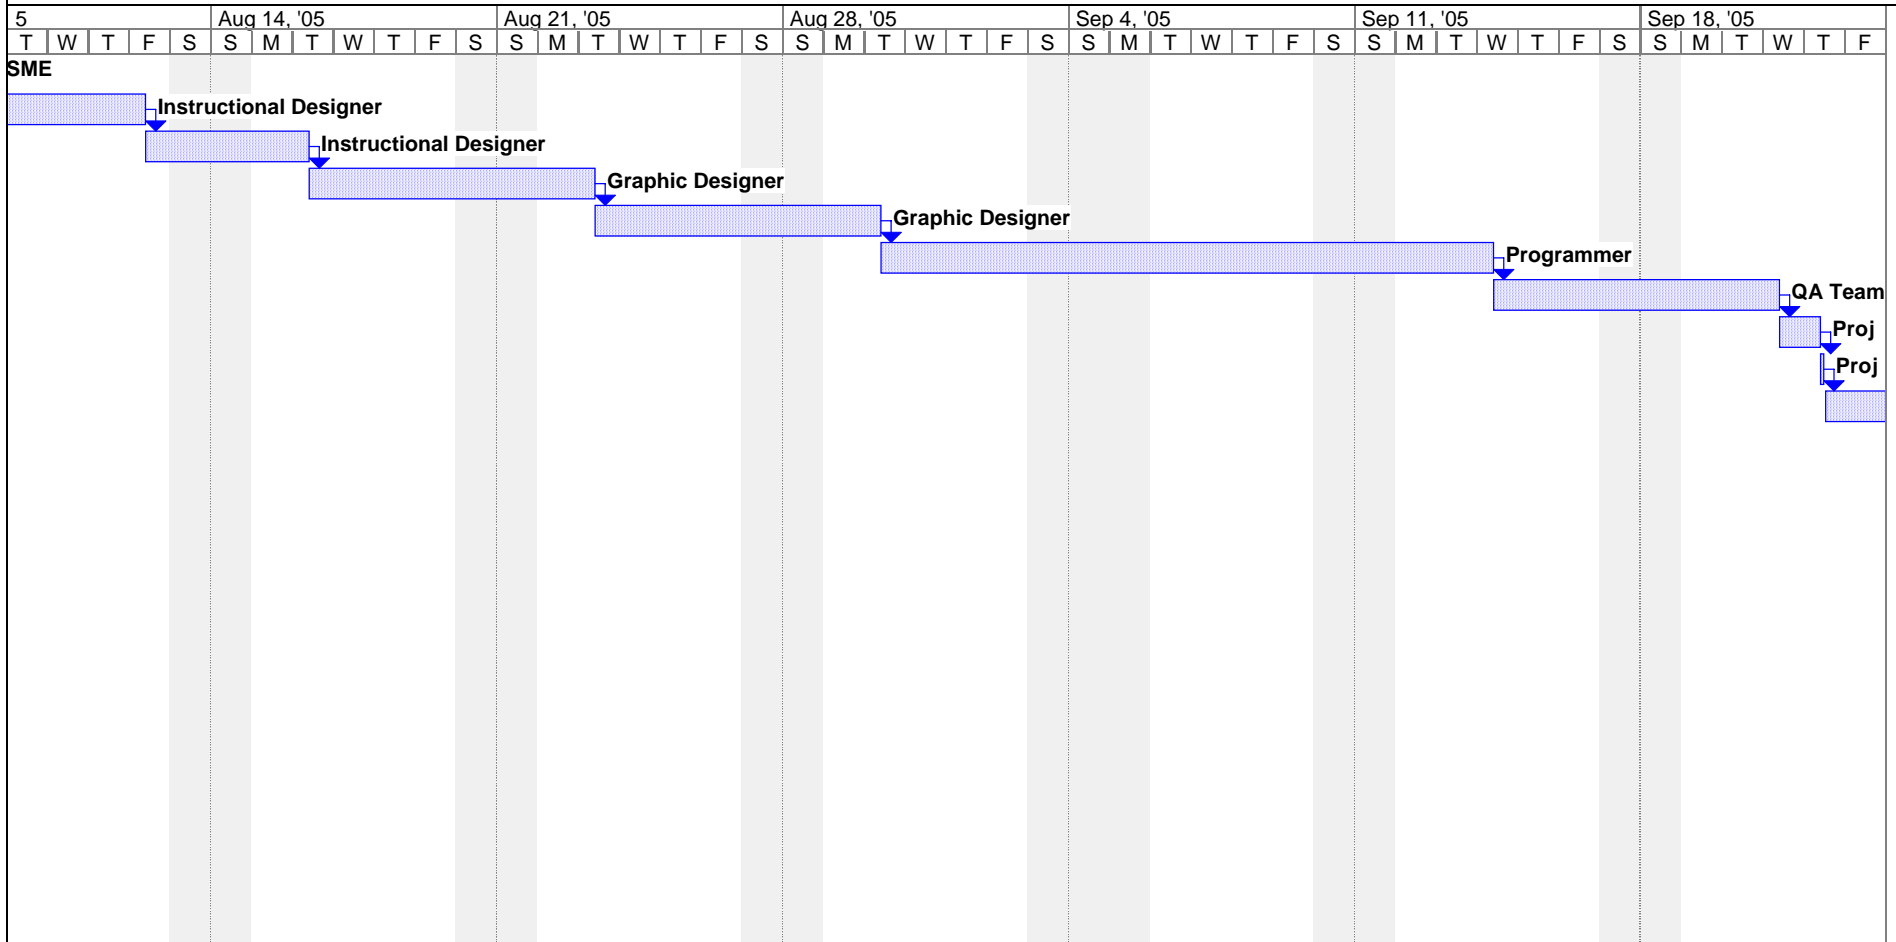

Project: project schedule Date: Wed 4/6/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

Sep 25, '05							Oct 2, '05							Oct 9, '05							Oct 16, '05							Oct 23, '05							Oct 30, '05							Nov 6, '05			
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="width: 20%;">Task</td> <td style="width: 20%;"></td> <td style="width: 20%;">Milestone</td> <td style="width: 20%;"></td> <td style="width: 20%;">External Tasks</td> <td></td> </tr> <tr> <td>Split</td> <td></td> <td>Summary</td> <td></td> <td>External Milestone</td> <td></td> </tr> <tr> <td>Progress</td> <td></td> <td>Project Summary</td> <td></td> <td>Deadline</td> <td></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

Sep 25, '05							Oct 2, '05							Oct 9, '05							Oct 16, '05							Oct 23, '05							Oct 30, '05							Nov 6, '05			
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

Project: project schedule Date: Wed 4/6/05	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

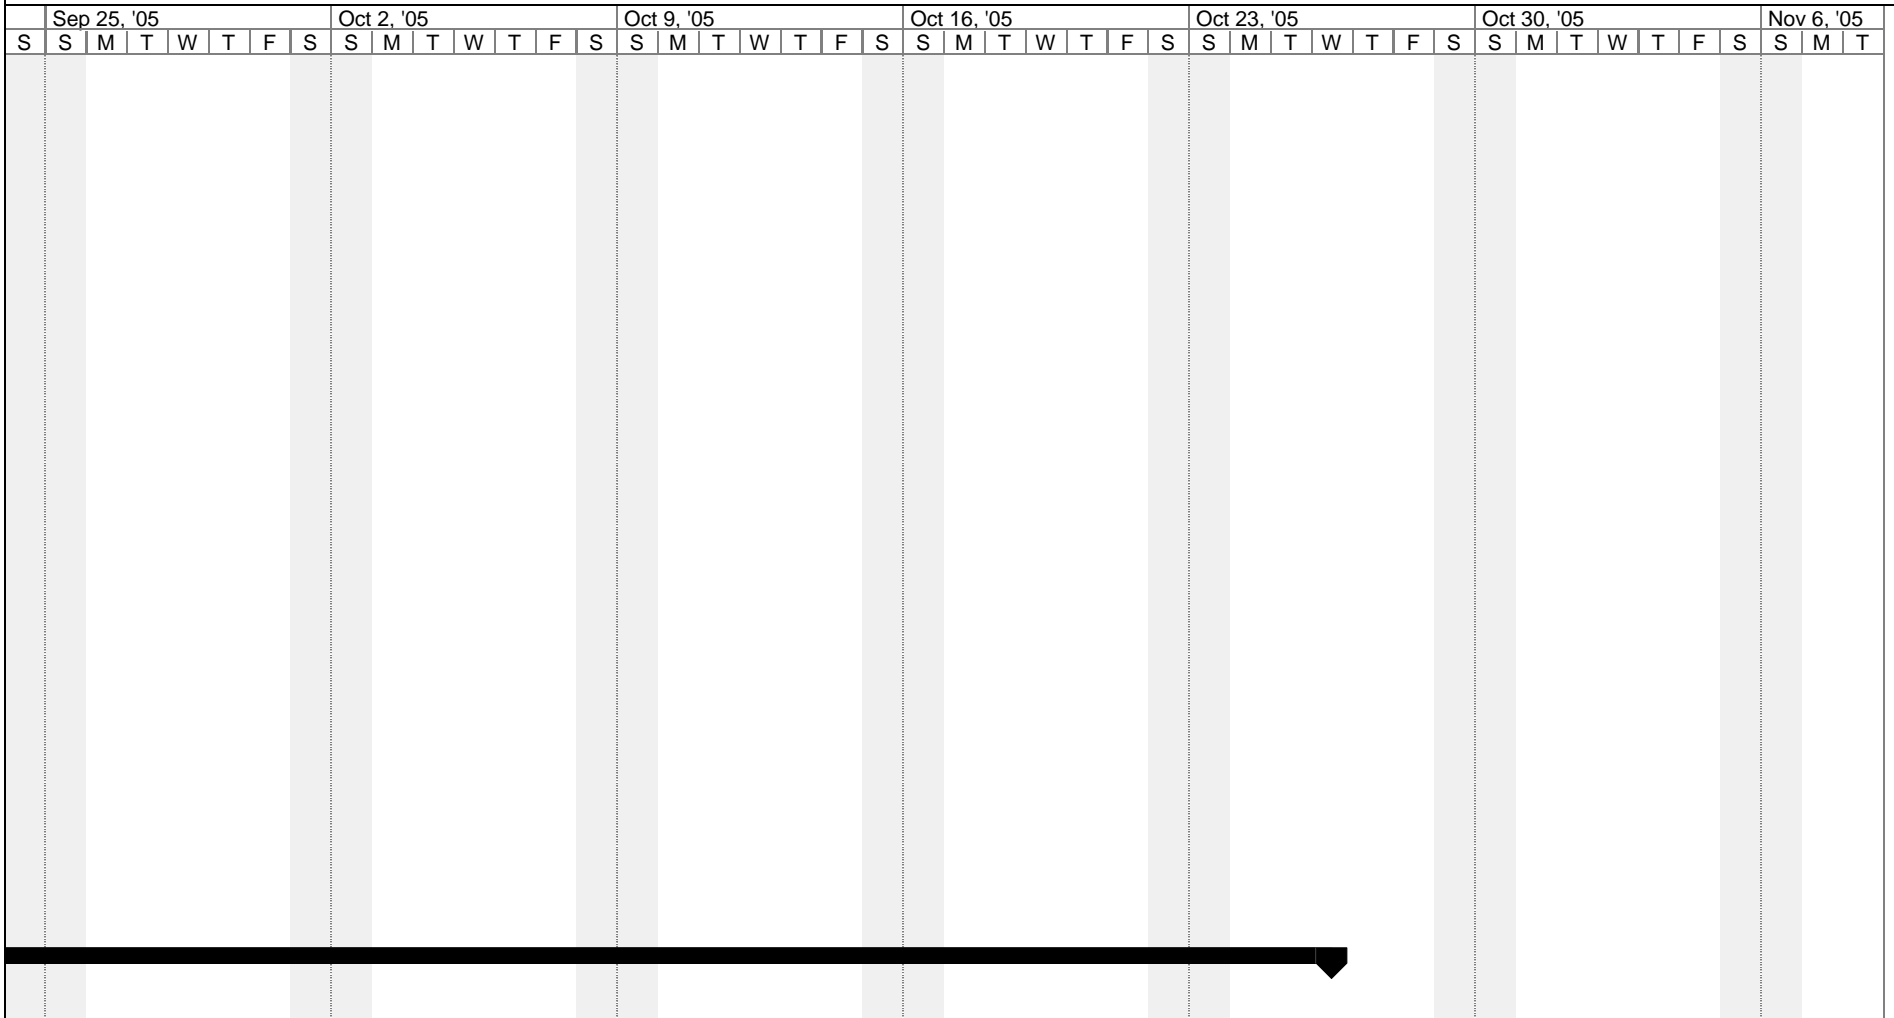

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="padding: 2px;">Task</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Milestone</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">External Tasks</td> <td style="padding: 2px;"></td> </tr> <tr> <td style="padding: 2px;">Split</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Summary</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">External Milestone</td> <td style="padding: 2px;"></td> </tr> <tr> <td style="padding: 2px;">Progress</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Project Summary</td> <td style="padding: 2px;"></td> <td style="padding: 2px;">Deadline</td> <td style="padding: 2px;"></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

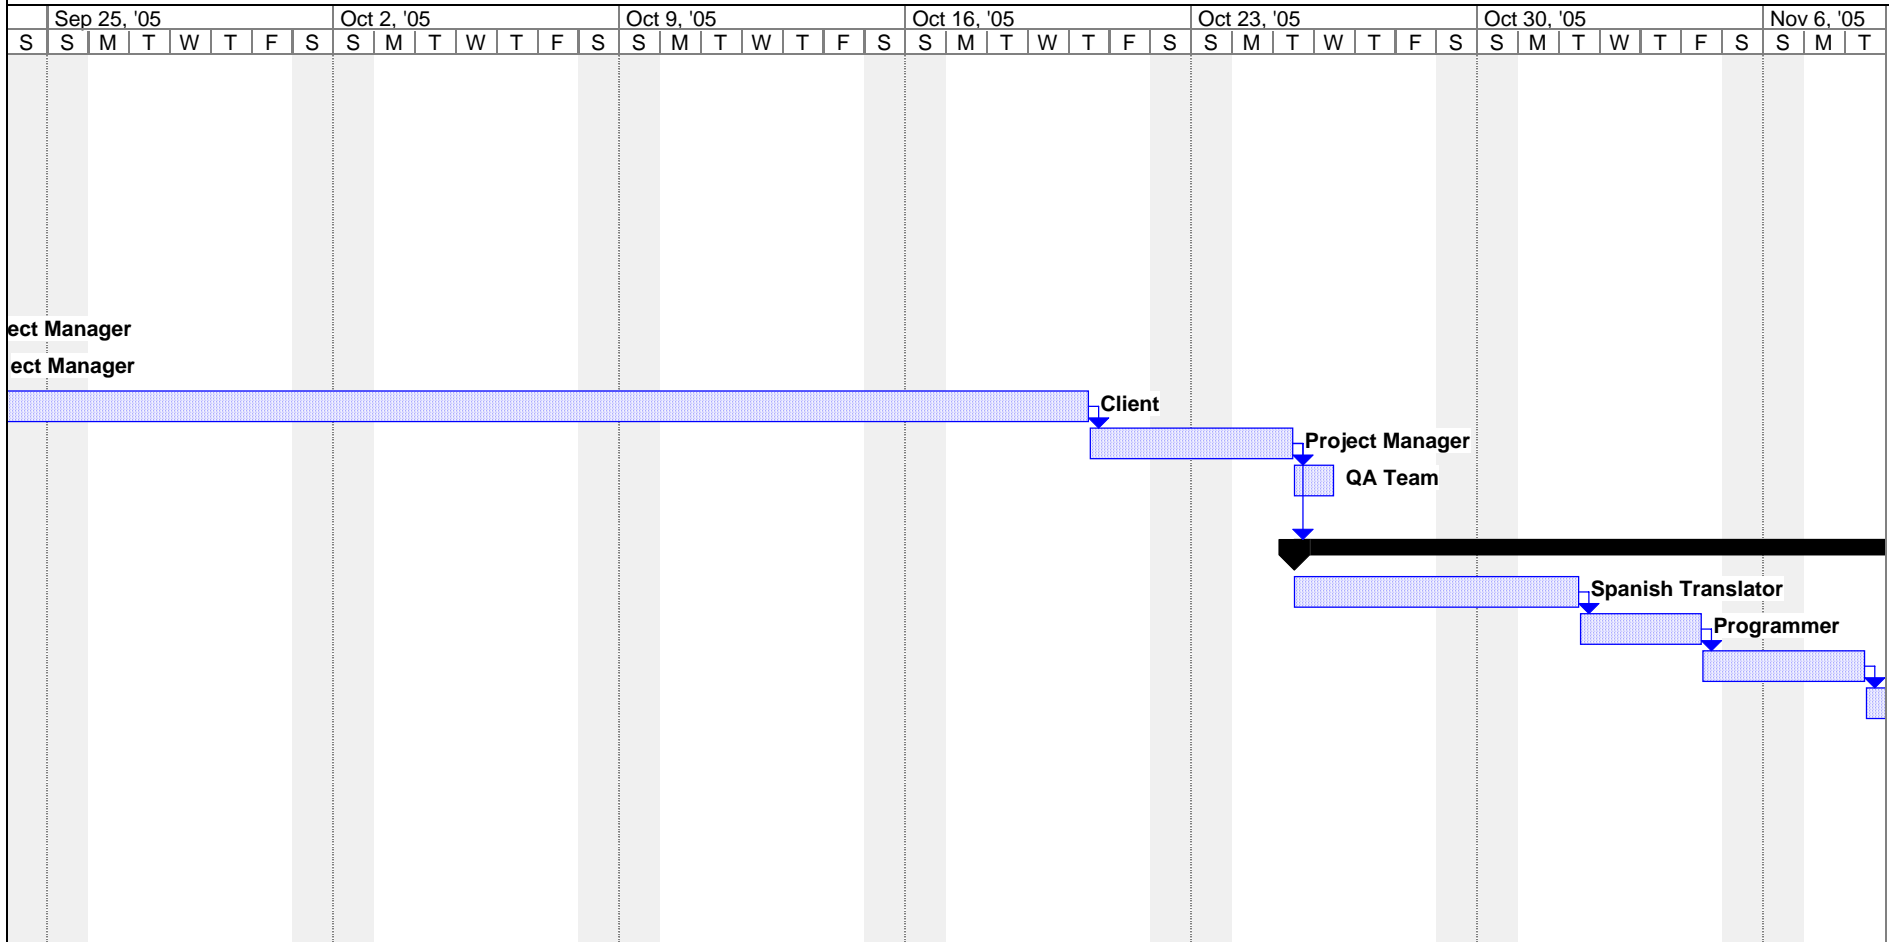

Project: project schedule Date: Wed 4/6/05	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

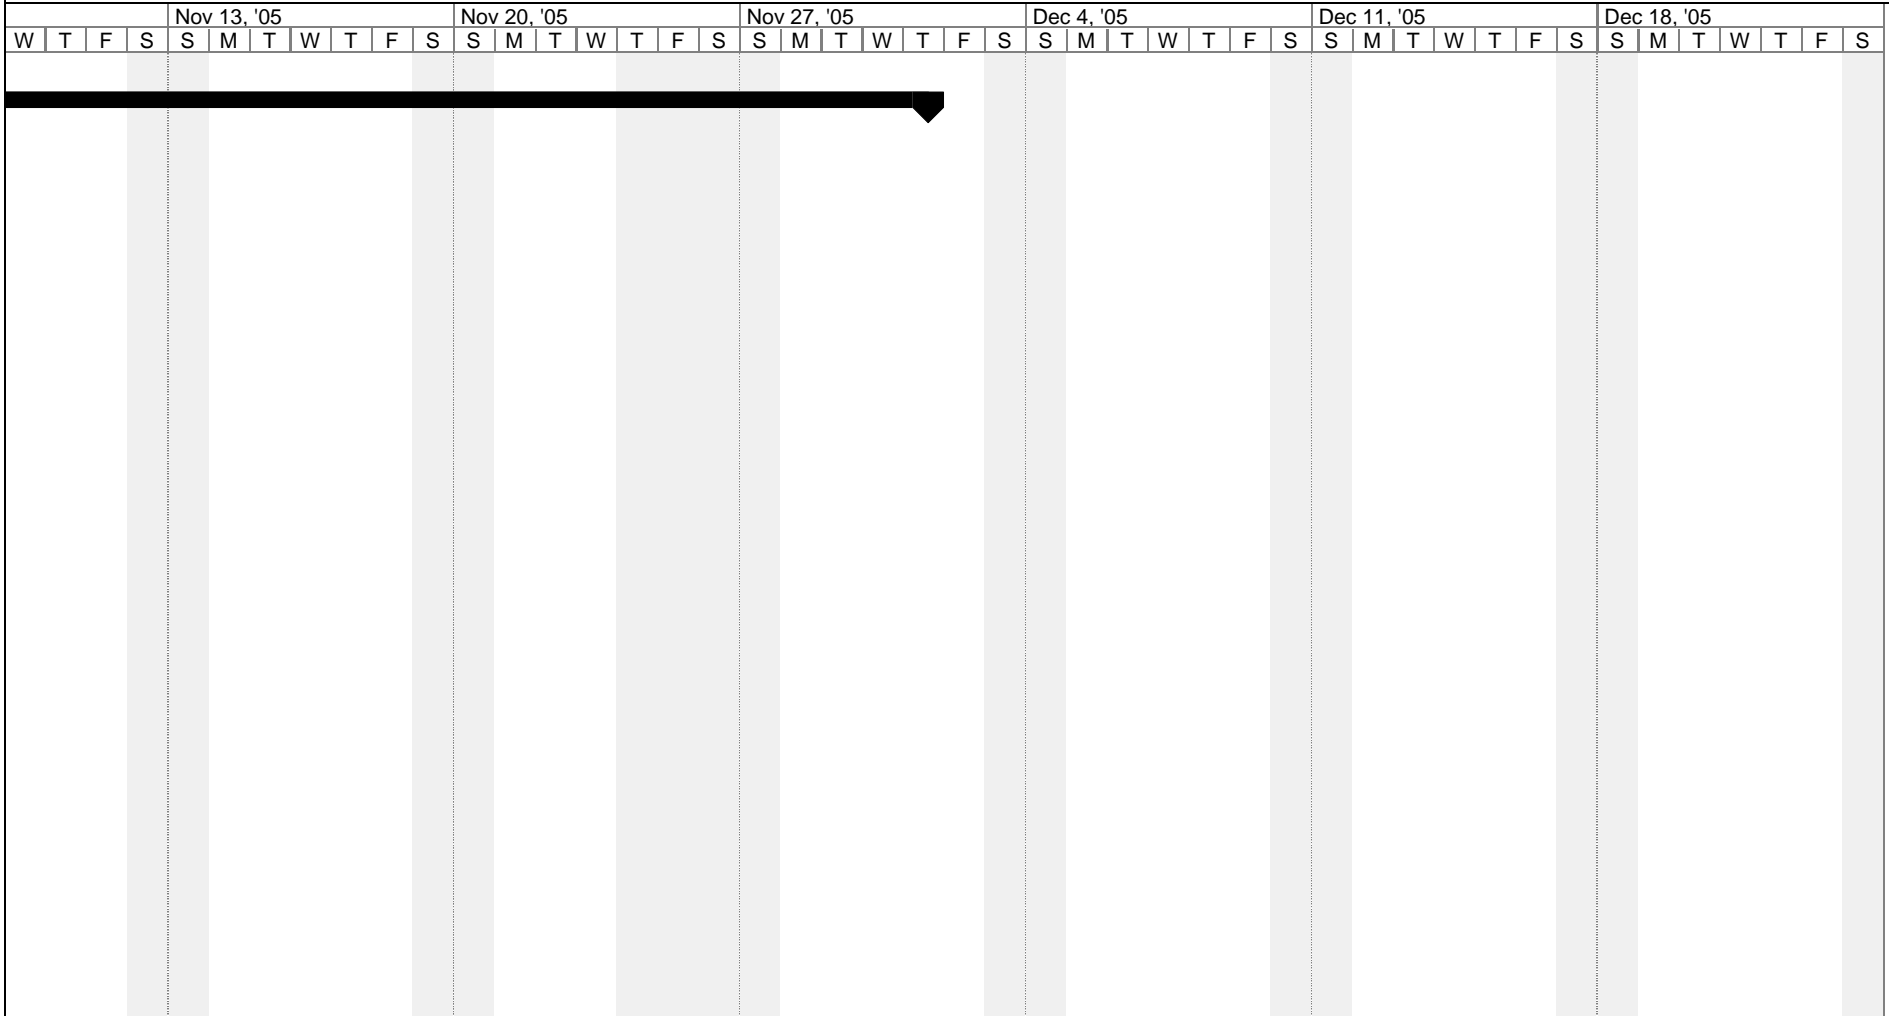




























Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Task</td> <td style="width: 15%;"></td> <td style="width: 15%;">Milestone</td> <td style="width: 15%;"></td> <td style="width: 15%;">External Tasks</td> <td style="width: 15%;"></td> </tr> <tr> <td>Split</td> <td></td> <td>Summary</td> <td></td> <td>External Milestone</td> <td></td> </tr> <tr> <td>Progress</td> <td></td> <td>Project Summary</td> <td></td> <td>Deadline</td> <td></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

Nov 13, '05				Nov 20, '05				Nov 27, '05				Dec 4, '05				Dec 11, '05				Dec 18, '05											
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="width: 15%;">Task</td> <td style="width: 15%;"></td> <td style="width: 15%;">Milestone</td> <td style="width: 15%;"></td> <td style="width: 15%;">External Tasks</td> <td style="width: 15%;"></td> </tr> <tr> <td>Split</td> <td></td> <td>Summary</td> <td></td> <td>External Milestone</td> <td></td> </tr> <tr> <td>Progress</td> <td></td> <td>Project Summary</td> <td></td> <td>Deadline</td> <td></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training


## Lifelong Knowledge & Research, Inc.

Nov 13, '05				Nov 20, '05				Nov 27, '05				Dec 4, '05				Dec 11, '05				Dec 18, '05											
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S

Project: project schedule Date: Wed 4/6/05	<table style="width: 100%; border: none;"> <tr> <td style="width: 20%;">Task</td> <td style="width: 20%;"></td> <td style="width: 20%;">Milestone</td> <td style="width: 20%;"></td> <td style="width: 20%;">External Tasks</td> <td></td> </tr> <tr> <td>Split</td> <td></td> <td>Summary</td> <td></td> <td>External Milestone</td> <td></td> </tr> <tr> <td>Progress</td> <td></td> <td>Project Summary</td> <td></td> <td>Deadline</td> <td></td> </tr> </table>	Task		Milestone		External Tasks		Split		Summary		External Milestone		Progress		Project Summary		Deadline	
Task		Milestone		External Tasks															
Split		Summary		External Milestone															
Progress		Project Summary		Deadline															

# Wallington Bank Leadership Skills Training

## Lifelong Knowledge & Research, Inc.

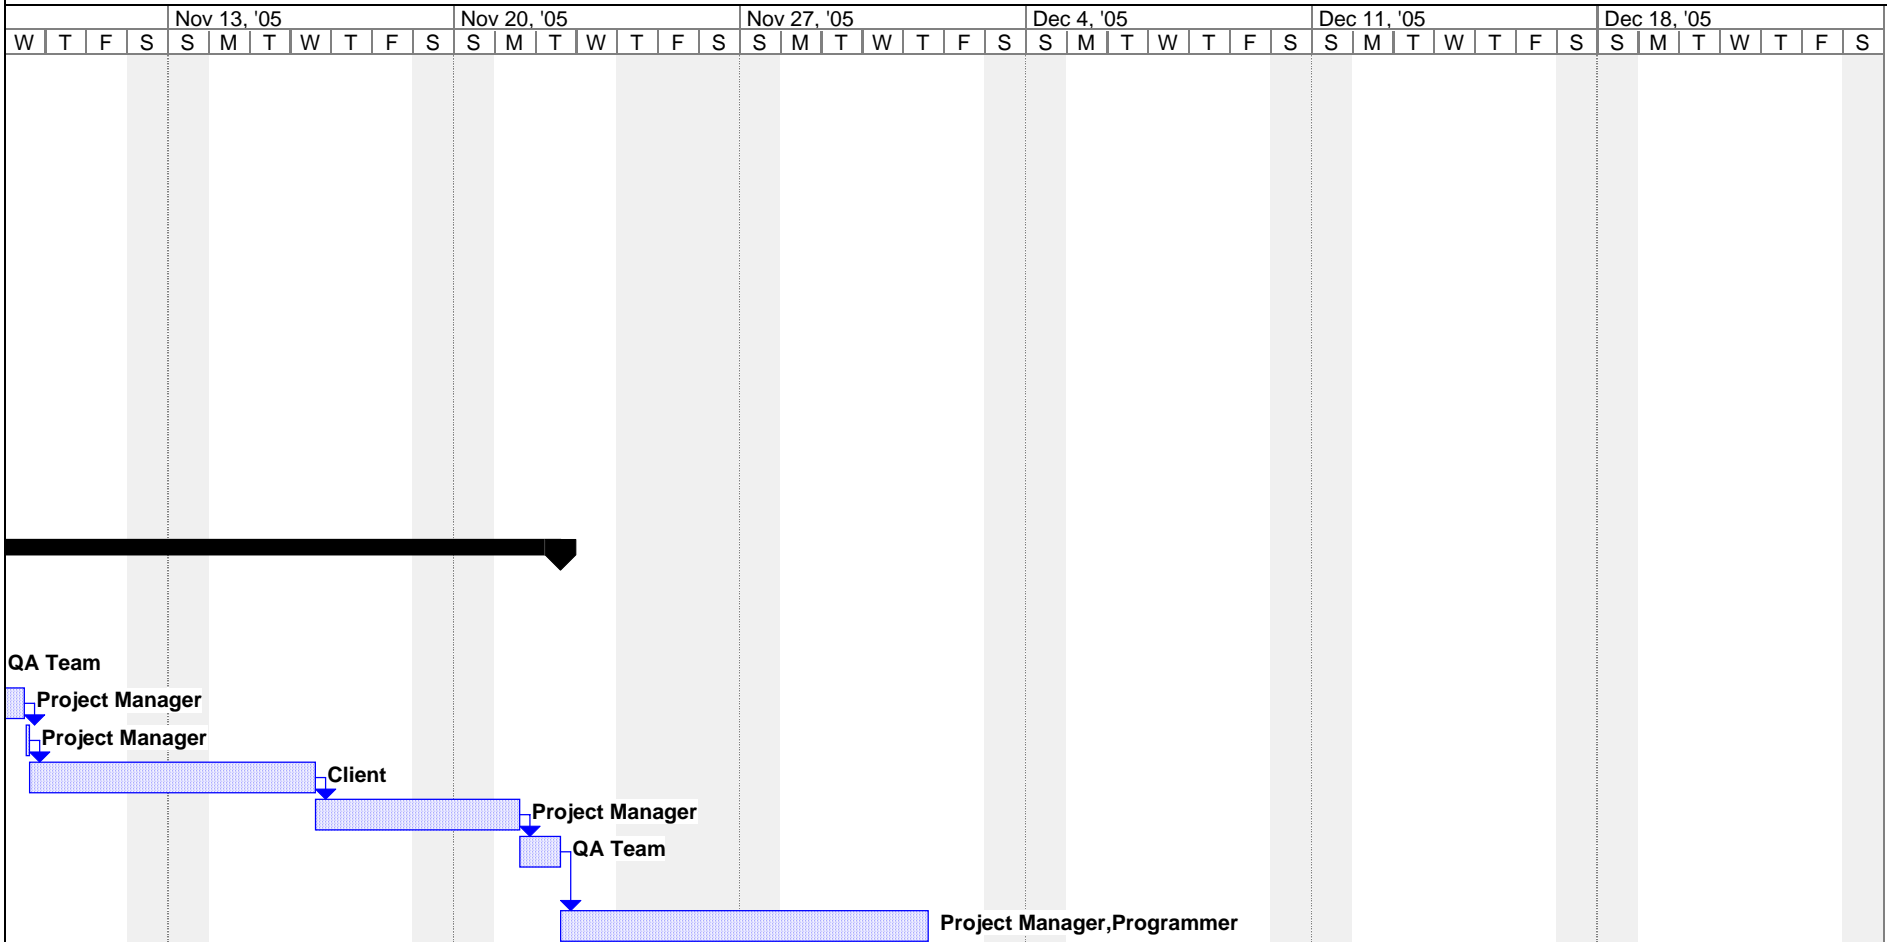

Project: project schedule  
Date: Wed 4/6/05

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
